

FIELD REPORT

201020047


Started... Aug... 29... 1978.

Completed Aug... 28... 1978.



NAME AND ADDRESS OF CLIENT	DESCRIPTION OF WORK	LOCATION OF WORK
[REDACTED]	WATER WELL	WATSON LAKE
[REDACTED] WATSON LANE		

FORMATION LOG			DESCRIPTION OF WORK	TIME			
FROM	TO	FORMATION		DATE	FROM	TO	HOURS
			MOVE				
29	30	GRAVLE		Aug 27	9	7	10
	30	GRAVLE & SAND		DRILL & CEASED WELL TO 41' 9"			
	34	SAND					
	36	GRAVLE		Aug 28	7	11:30	4.5
	38	ROCKY GRAVLE		INSTALLED SCREEN			
	40	TILL		BACK WASHED & AIR DEVELOPED			
				DEVELOPING 2 HR.			

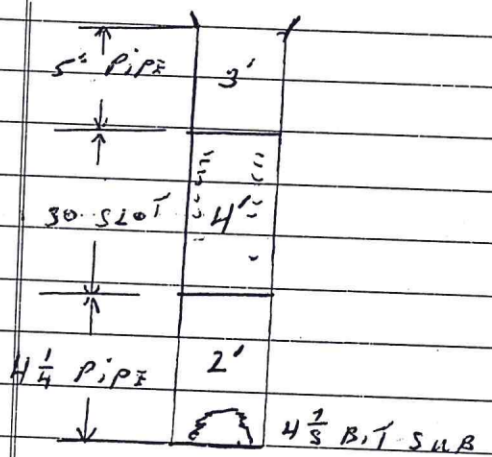

Type of Casing & Pipe		
Type	Size	Type
Inch	Feet	Inch
1 1/2		
9 1/2		
9		
0		
9'		

Remarks: TOP OF SCREEN 35.4
 30 SLOT SCREEN 39' 4" BOTTOM
 BOTTOM WELL 41' 4"
 AIR DEVELOPED TO 10 G.P.M.
 Pump 502 AT 34' L'
 MUD C 44420 K.A.P. 220 VOLT 1 OUR 500# 8-83

STATIC LEVEL	AIR DEVELOPING 2 HR.
Ground level	Total Rig Time 11.5 hrs.
Top of casing 20' 10"	Total Standby hrs.
	Drilling Mud 9 sacks

MIDNIGHT SUN... [REDACTED] SIGNATURES
 CLIENT.....
 TITLE.....
