




PROJECT: <b>ERDC Site Wide Monitoring Plan (13 002-4)</b>	BORING ID: <b>KAR13-008</b>	
LOCATION: <b>Keno Hills Silver District (KHSD)</b>	WELL ID: <b>Husky SW (Completed)</b>	
DRILLING CONTRACTOR: <b>Access Consulting Group</b>	NORTHING: <b>7086594</b>	EASTING: <b>473893</b>
DRILLING EQUIPMENT: <b>Midnight Sun Drilling Inc.</b>	GROUND SURFACE ELEV. (masl): <b>736</b>	TOC ELEVATION (m ags): <b>0.74</b>
DRILLING METHOD: <b>Air Rotary</b>	TOTAL DEPTH (m): <b>14.02</b>	WATER DEPTH (m bgs): <b>7.89</b>
SAMPLING METHOD: <b>2 Feet (0.61 m) Continuous Sampling</b>	DATE STARTED: <b>September 1, 2013</b>	DATE COMPLETED: <b>September 2, 2013</b>

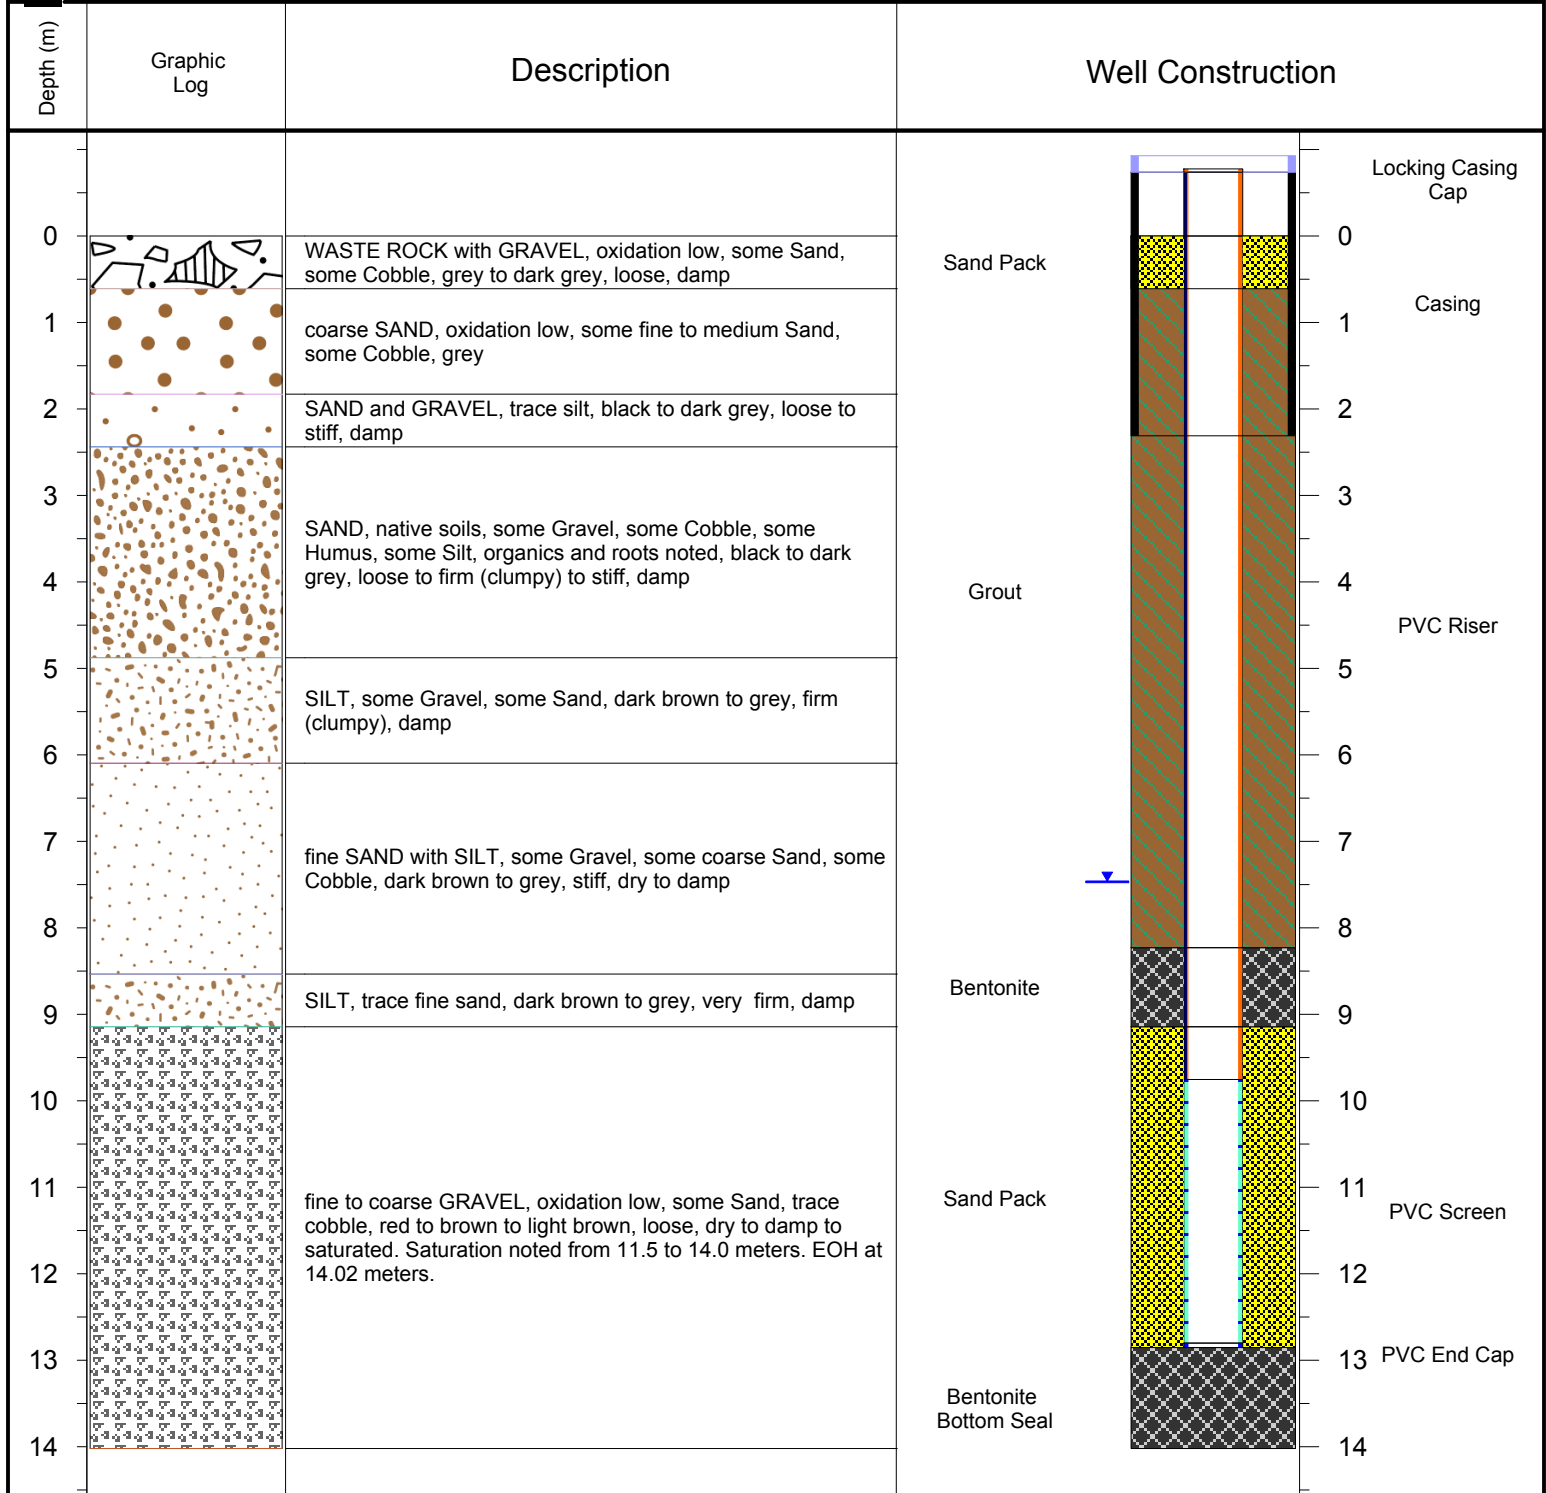

NOTES: Wells are 2 inches in diameter.  
EOH @ 14.02 m.  
Well depth is 12.8m. 1.22m of bentonite was used as a bottom seal.
