


HYDROGEOLOGIC LOG

BOREHOLE NO.

WELL 3964/3121-B

PURPOSE OF HOLE: Water Supply Well
 DRILLING METHOD: Dual Air Rotary
 START DRILLING: Sept 16, 2007
 SCREEN INTERVAL: 58.3 m - 59.5 m
 CONTRACTOR: Double 'D' Drilling Ltd.

CASING STICK UP (m): 1.0 m above grd.
 DEPTH TO STATIC (m): 14.7 m below grd.
 DEPTH TO SCREEN TOP (m): 58.3 m

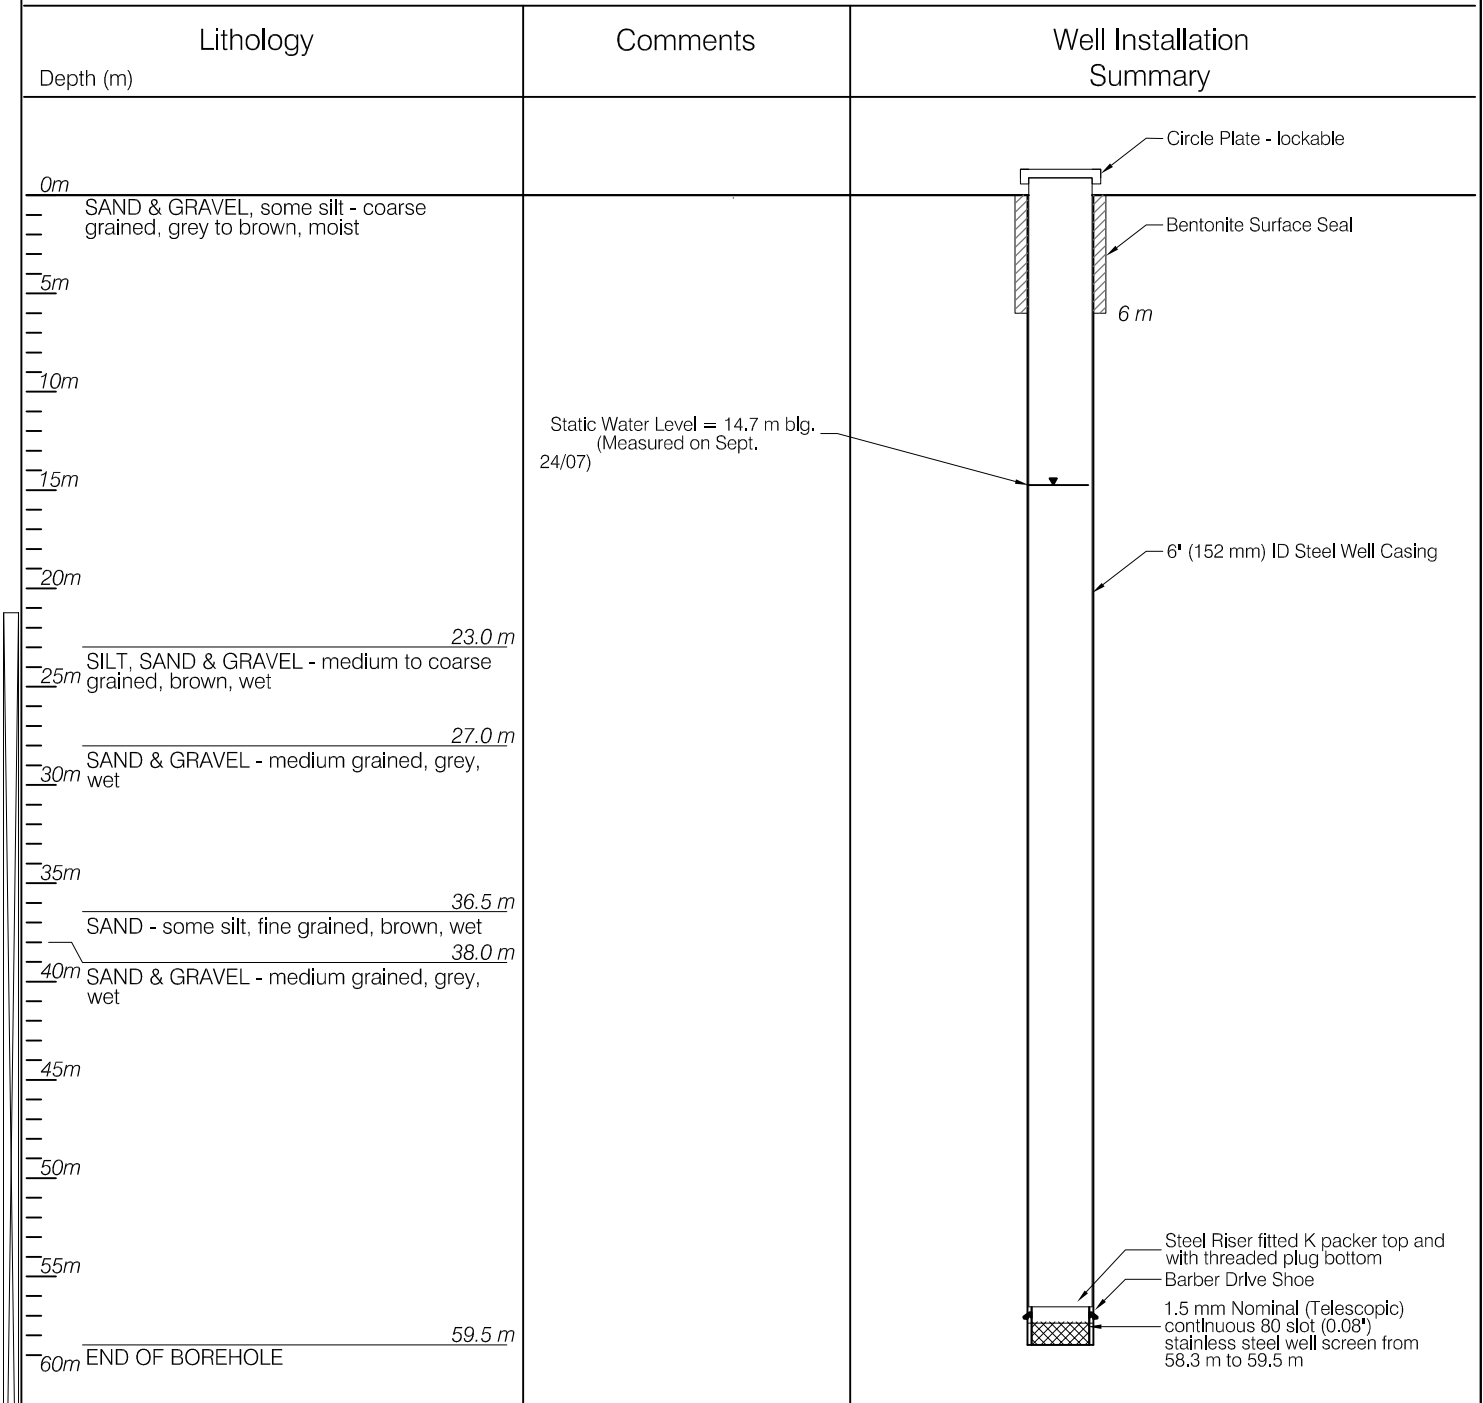

<p>CLIENT</p>	<p>Water Well Completion Report Health and Visitor Centre Wells 3964 & 3121 Beaver Creek, YT</p>			
<p>EBA Engineering Consultants Ltd.</p>	<p>SITE PLAN AND WELL LOCATIONS</p>			<p>PROJECT NO. W23101031</p> <p>DIVN JSB</p> <p>CKD TAK/RMM</p> <p>REV 0</p> <p>DATE October 31, 2007</p> <p>Figure 3</p>
