Project Name: Supplemental Phase II / III ESA **Test Hole ID:** **MW19-08**
Project Number: [redacted] **Site Location:** Carmacks Highway Maintenance Yard

Coordinates

Easting: 433334.226
Northing: 6885065.557
Datumn: NAD83 UTM Zone 08N

Drilling Details

Drill Contractor: [redacted]
Drill Date: **August 7, 2019**
Drill Method: **Sonic**
Maximum Drilled Depth (mbgs): **6.10**
Drillhole Diameter (mm): **152**

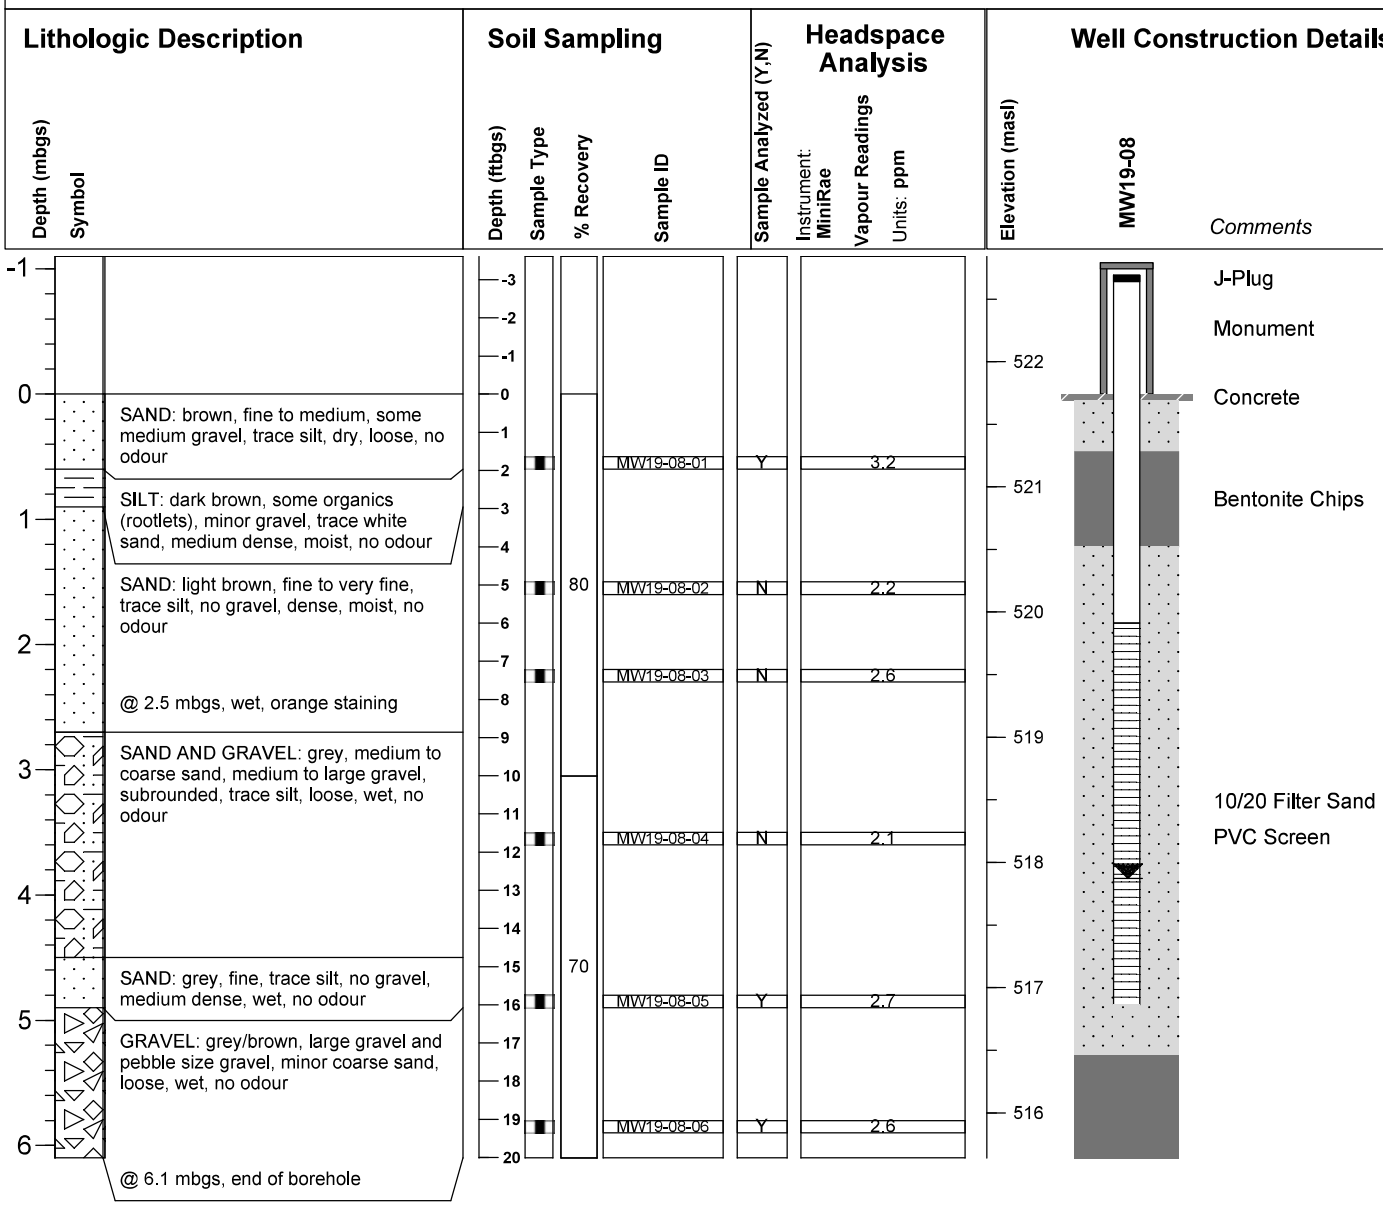

core6 ENVIRONMENTAL

Report Date: **August 2019**
Logged by: [redacted]
Approved by: [redacted]
Client: **Yukon Government**

MW19-08
Top of Casing Elevation (masl): **522.725**
Ground Elevation (masl): **521.74**
Screen Interval (mbgs): **1.83 - 4.88**
Depth to Bottom (mbTOC): **5.64**
Depth to Water (mbTOC): **3.869**
Water Level Date: **August 13, 2019**
Casing Diameter (in): **2**
Screen Slot Size: **10**
Casing Material: **PVC**
